

AstraX EB1 Integration – Critical Path to Completion

TARGET: JULY 15, 2026

A structured, sequenced execution plan governing hardware readiness, mechanical delivery, and full system integration. Over 70% of schedule risk is concentrated in the Electrical Path — controlled execution guarantees EB1 delivery on time.

⚙️ Electrical Backbone

Critical — RED

- PCB Fabrication: Apr 30 → May 30
- Board Bring-Up: Jun 1 → Jun 15
- System Interconnect: Jun 15 → Jun 22

🔧 Mechanical Track

Parallel — AMBER

- Mechanical Fabrication
- Assembly & Debug
- HH Assembly Shipment

🔗 System Integration


Critical — RED

- Install Working PCBs: Jun 29 → Jul 5
- System Test & Debug: Jul 5 → Jul 15

⚠️ Execution Risks

Concentration Points

- PCB Vendor Delay = Full Schedule Slip
- Bring-Up Complexity (FW + HW coupling)
- Integration depends on dual-track sync

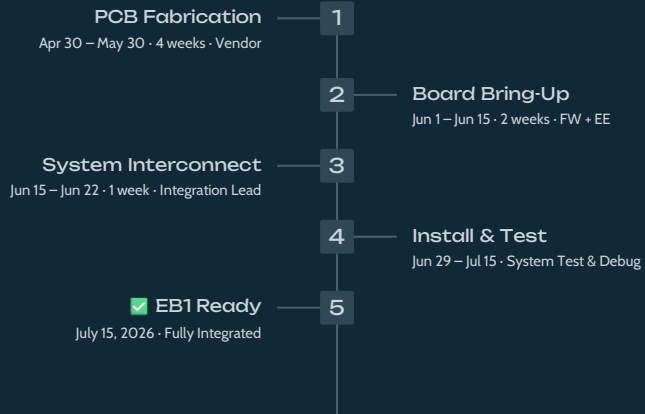


Hardware Readiness Backbone governs the entire schedule. Parallel mechanical execution enables integration — both tracks must synchronize at the Jun 29 install gate to protect the July 15 milestone.

EB1 Execution Risk Heatmap

IMPACT VS. LIKELIHOOD

All material execution risks have been identified, categorized, and assigned active mitigations. No unknown execution variables remain. The top three risks are owned and actively tracked through daily war-room controls.

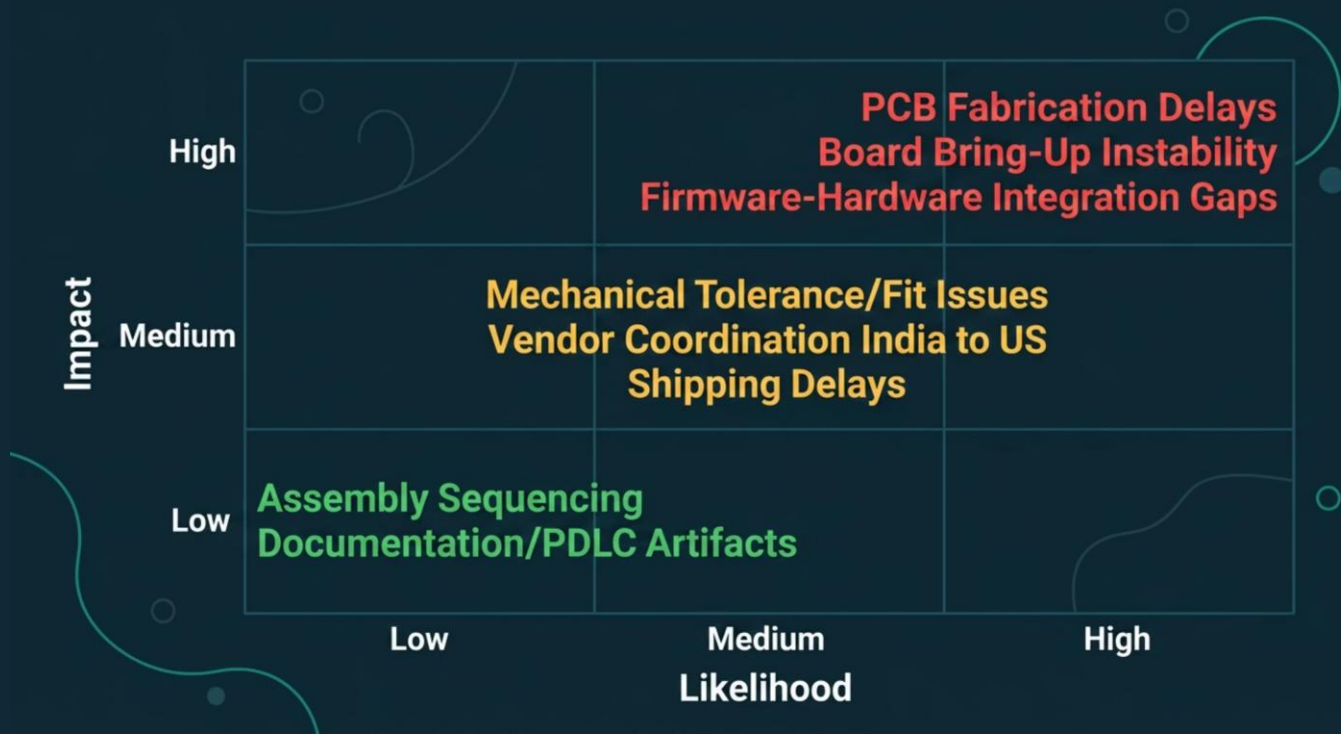

● High Risk — Owned

- PCB Fabrication Delays
- Board Bring-Up Instability
- Firmware-Hardware Integration Gaps

Active Mitigations

- Daily Vendor Tracking — War Room cadence with PCB supplier
- Parallel Execution Strategy — Mechanical track runs concurrent to prevent bottleneck

EB1 Execution Command Center

90-DAY WAR ROOM DASHBOARD

Execution is no longer conceptual — it is structured, measurable, and tightly controlled. Every phase is tracked with a clear owner, RAG status, and completion percentage. Gate reviews enforce discipline at every critical handoff.

Phase Status Tracker — RAG

Phase	Status	Owner	Completion	Next Gate
Electrical Fabrication	Critical	Vendor	40%	May 30
Board Bring-Up	In Progress	FW + EE	20%	Jun 15
Mechanical Assembly	On Track	Steve Team	60%	Jun 22
System Integration	Not Started	Vijay	0%	Jun 29

1 Daily War-Room Controls

 **Daily**
PCB Vendor Status Check · Issue Escalation

 **Weekly**
Cross-functional Sync · Integration Readiness Review

 **Gate Reviews**
Design Freeze ✓ · Bring-Up Gate · Integration Gate

Bottom-Line KPIs

Jul 15

Target Date
2026 delivery commitment

~7d

Buffer Available
5–7 days schedule reserve

HIGH

Confidence
Controlled critical path

"Execution is no longer conceptual — it is structured, measurable, and tightly controlled to deliver EB1 on schedule."
